

# Fox Cities Exhibition Center

## Weekly Update - 04/24/2017

---


### Key Progress Points

- ◇ **Radisson Paper Valley Hotel Work:** *Work began this week on relocating the existing chiller lines at the Radisson Paper Valley Hotel. The mechanical contractor worked on running the new pipe beneath the building, as well as installing the valves to divert the piping. Excavation and laying of the new pipe across the alleyway behind the hotel will happen in the coming week.*
  
- ◇ **Excavation/Tieback Anchors/Pipe Piles:** *Testing of the tieback anchors continued this week, as well as installing the pipe piling. The crews primarily focused on the piling and were able to get everything driven up to the east side of the building footprint. Excavation crews continued to work hand-in-hand with the pipe piling and concrete crews to remove soils for grade beams and pile caps.*
  
- ◇ **Concrete:** *The northeast corner of the building was formed and rebar installed in preparation for a concrete pour on Saturday. This corner of the building is the most complicated, so extra attention was given to ensure everything was perfect before the pour. Work also continued on the grade beams and pile caps along the west and south sides of the jobsite.*
  
- ◇ **Conditions & Safety:** *Rains came periodically throughout the week. The weather did not cause any delays in the schedule, but resulted in the crews rearranging concrete pours throughout each day. No injuries occurred this week.*

## Progress Photographs



Rebar crews working on installing the rebar along the northeast corner of the building.

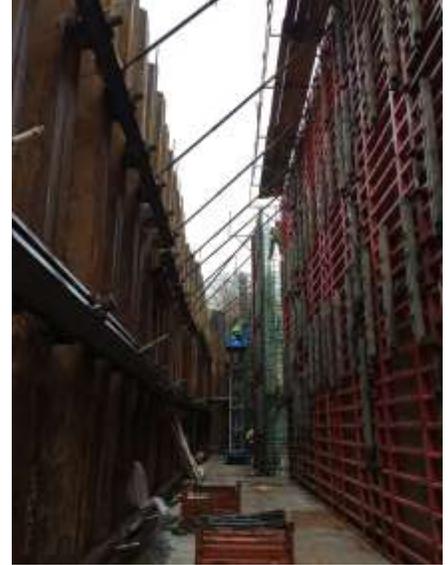

This area is in between the sheet piling and the exterior of the concrete walls. A thinner concrete mat was poured in this area to provide easy mobility for the crews.



Concrete being poured into the pile caps and grade beams for the interior walls of the exhibition hall.



Crews working on the interior grade beams and pile caps with the finished freight elevator shaft in the background.
